
Bi weekly Field Report

Surveyor Date visited Time visited Zaw La 7 Feb 2019 15:30 pm

Weather Condition Sunny
The last time of heavy raining:

No	Item	Condition	Narrative Description and Photos	
1	(1.1) Water Supply System	Improved □ Same ■* Worse □ *as last week	Narrative Description Water distribution system has been surzone B resettled families. The new we line and its necessary instruments becaprevious well includes iron hydroxide the iron removal tank. The current wat iron hydroxide and yellowish mud are	Il was drilled and installed the pipe ause the underground water of the and yellowish mud that clogged in ter condition is quite good and no
			Photos	
			Water from ground water tank	Pipe line distribution water to houses

No	Item	Condition	Narrative Description and Photos	
1	(1.2) Well	Improved□ Same •* Worse □ *as last week	living. There are eleven tube well the water basically from the pip frequency of water usage from the	lean enough to use for drinking and ls in the relocation site. Residents use beline distribution system so that the he tube wells is very low. To sustain wells, the leg pumps were kept and aps till the residents use.
			Open Well No. 1	Open Well No. 2
	(2) Drainage	Improved□ Same ■* Worse □ *as last week	The drain at the corner of Main Road A and B The exit of the drain at the corner of Site village road and 3 rd street	The exit of the drain at the corner of Site village road and 2 nd street The exit of the drain at the corner of Site village road and Main Road C
	(3) Road	Improved□ Same © *	All the roads are getting dry an	nd no problem for walking.
		Worse □	Photos	

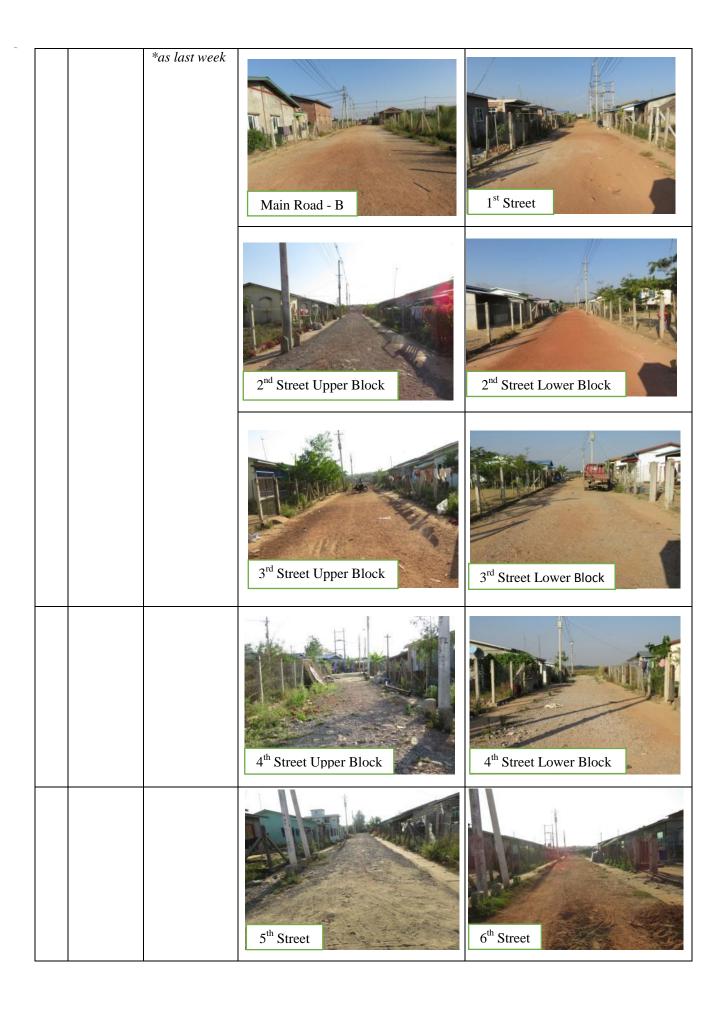

(4)	Improved□	7 th Street The rubbish was dumped at the co	Site Village reek side and even in front of the
Garbage Condition	Same ●* Worse □ *as last week	of each road until the end of Apri are kept by the community leader near the triangle junction of Main	been provided and placed at the corner l. After April 2018, all the garbage bins of PAPs in the communal compound a Road C and Upper Fourth Street. But e truck from township municipal office
		Rubbishes in the creek near 1st street	Rubbishes in the creek near 2nd street
		Rubbishes in the creek near Main Road C	Rubbishes in the creek near 6 th Street

(5) Fly	
proof	
toilet	

Improved□ Same ■* Worse □ *as last week

- All of the fly proof toilets are used the residents.
 - All of the toilets are repaired by the following procedures;
 - Installation the extra septic tanks beside the original
 - The pipe line system is installed from the extra tank to the ditch to flow the liquid out.

The toilet renovation plan was successfully done and there is no problem at the moment.

	No. of HHs		
Condition	This week condition	Previous	
		week condition	
Level 1	91	91	
Level 2	0	0	
Level 3	0	0	
Level 4	0	0	
No Toilet	0	0	

<Evaluation Criteria>

Level 1

- Fly proof toilet is not needed to be repaired.
- No/rarely toilet unavailable

Level 2

- Fly proof toilet is needed to be repaired.
- Rarely toilet unavailable

Level 3

- Fly proof toilet is needed to be repaired.
- Often toilet unavailable
- As the result of filling the soil and also due to the heavy rain, some toilets are inconvenience to use.

Level 4

- Fly proof toilet is urgently needed to be repaired.
- Often toilet unavailable

Photos









	(6) Electricity	Improved□ Same ■* Worse □ *as last week	 Residents get the electricity regularly. Electric poles and transformer are being supported with the good foundations. There are some pieces of wood under an electric pole of main road B and it's needed to clean up. Photos Transformer No. 1 Transformer No. 2 Electric poles of Main Road B and Main Road C
No	Item	Condition	Description and Photos
2	(1)House Construct- ion	No. of houses which are not completed (4)	 In plot No.9 and 10, three houses that are planned to build as the plots are owned by father and son. Construction has been finished for two houses and one house is not finished yet. Plot No.64, the house construction seems to be stopped. Plot No.78, the house construction is needed to be carried on, however PAPs are living now. Plot No. 66, the house construction for the first floor has been finished and the second floor is still needed to be carried on.
			Photos
			House No. 9 House No. 64





3 Other Issues

(1). Drainage condition for rain water in the compounds

Description

	No. of HHs	
Condition	This week	Previous week
	condition	condition
Level 1	85	85
Level 2	6	5
Level 3	0	0
Level 4	0	1

<Evaluation Criteria>

Level 1

-No mud and no standing water with their own drainage system in their compound

Level 2

-No mud and no standing water in their compound


Level 3

- Some or little mud and standing water in their compound

Level 4

-A lot of mud and standing water in their compound

Photos

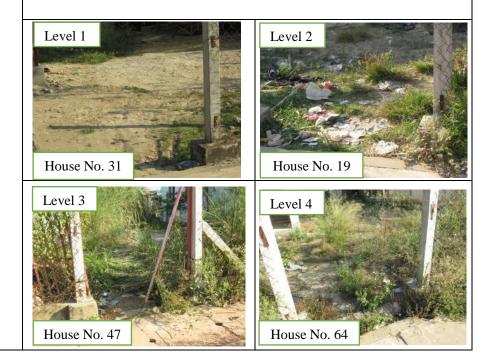



(2) Plantation

In front of the compounds, the shady trees, fruit trees, flowering plants and vegetables are being planted.

Description

- In front of the compounds, the shade trees, fruit trees, flowering plants and vegetables are being planted.

Type	No. of HHs	Remarks
Shade tree	15	Albizzia, Indian almond, Neem tree, etc. HH No. 20, 40, 43, 48, 51, 57, 59, 61, 62, 67, 69, 72, 73, 77, 85
Fruit tree	37	Banana, Mango, sugar cane, coconut, citrus and jack fruit etc. HH No. 3, 15, 17, 20,21, 23, 28, 30, 31, 32, 34, 37, 40, 41, 48, 51, 52, 55, 57, 58, 59, 61, 62, 63, 67, 68, 70, 71, 72, 73, 77, 78, 82, 85, 86, 88
Vegetables	20	Chili, tomato, bitter gourd, Roselle, gourd, basils, eggplant etc. HH No. 12, 17, 21, 41, 49, 58, 59, 61, 62, 63, 67, 68, 70, 71, 72, 73, 77, 82, 85, 86
Flowering plant	31	Jasmine, poinsettia, orchid, kiss me quick, etc. HH No. 3, 5, 6, 8, 10, 12, 13, 14, 17, 20, 21, 22, 23, 29, 30, 31, 32, 46, 48, 58, 59, 61, 62, 65, 67, 68, 69, 72, 77, 78, 86

Photos,









(3) Livestock

Description

-The chicken, gooses and ducks are being raised.		
No. of HHs	Remarks	
6	HH No. 13, 14, 21,	
	59, 67, 78	
3	HH No.12	
2	HH No. 40, 67	

Photos



