Bi weekly Field Report

Surveyor Date visited


Time visited

Zaw La 18 Jul <u>2019</u> <u>15:30 am</u>

Weather Condition <u>Cloudy</u>
The last time of heavy raining: Yesterday

No	Item	Condition	Narrative Description and Photos		
1	(1.1) Water Supply System	Improved □ Same ■* Worse □ *as last week	Narrative Description Water distribution system has been supporting ninety household of the zone B resettled families. The new well was drilled and installed the pipe line and its necessary instruments because the underground water of the previous well includes iron hydroxide and yellowish mud that clogged in the iron removal tank. The current water condition is quite good and no iron hydroxide and yellowish mud are found.		
			Photos		
			Water from ground water took	Dies line distribution water to hove	
			Water from ground water tank	Pipe line distribution water to houses	

No	Item	Condition	Narrative Description and Photos		
1	(1.2) Well	Improved□ Same ■* Worse □ *as last week	 Water from two open-wells is clean enough to use for drinking and living. There are eleven tube wells in the relocation site. Residents use the water basically from the pipeline distribution system so that the frequency of water usage from the tube wells is very low. To sustain the good condition of the tube wells, the leg pumps were kept and covered the PVC pipes with the caps till the residents use. 		
			Open Well No. 1	Open Well No. 2	
	(2) Drainage	Improved□ Same ■* Worse □ *as last week	The drain at the corner of Main Road A and B	The exit of the drain at the corner of Site village road and 2 nd street	
			The exit of the drain at the corner of Site village road and 3 rd street	The exit of the drain at the corner of Site village road and Main Road C	
	(3) Road	Improved□ Same ■* Worse □ *as last week	All the roads except 6 th street are still dry and no problem for walking. 6 th street is being damaged due to passing the heavy trucks that carry the soil to fill near the creek side. Therefore the exits of the drain at the 6 th street are being blocked with the soil.		
		<u>Photos</u>			

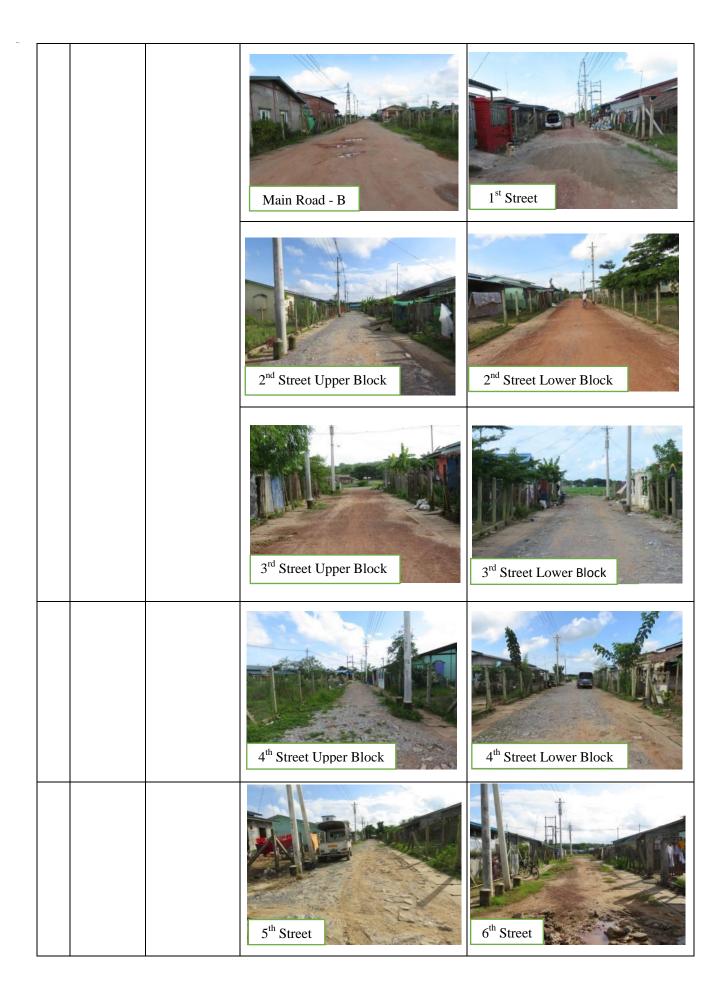

(4)	Improved□	7 th Street The rubbish was dumped at the cr	Site Village reek side and even in front of the
Garbage Condition	Same ■* Worse □ *as last week	of each road until the end of Apri are kept by the community leader near the triangle junction of Main	been provided and placed at the corner l. After April 2018, all the garbage bins of PAPs in the communal compound a Road C and Upper Fourth Street. But e truck from township municipal office
		Rubbishes in the creek near 1st street	Rubbishes in the creek near 2nd street
		The soil was filled near the creek of Main Road C in March	The soil was filled near the creek of 6 th Street in March

(5) Fly	
proof	
toilet	

Improved□
Same ■*
Worse □
*as last week

- All of the fly proof toilets are used the residents.
 - All of the toilets are repaired by the following procedures;
 - Installation the extra septic tanks beside the original
 - The pipe line system is installed from the extra tank to the ditch to flow the liquid out.

The toilet renovation plan was successfully done and there is no problem at the moment.

	ΙΗs	
Condition	This week condition	Previous
		week condition
Level 1	91	91
Level 2	0	0
Level 3	0	0
Level 4	0	0
No Toilet	0	0

<Evaluation Criteria>

Level 1

- Fly proof toilet is not needed to be repaired.
- No/rarely toilet unavailable

Level 2

- Fly proof toilet is needed to be repaired.
- Rarely toilet unavailable

Level 3

- Fly proof toilet is needed to be repaired.
- Often toilet unavailable
- As the result of filling the soil and also due to the heavy rain, some toilets are inconvenience to use.

Level 4

- Fly proof toilet is urgently needed to be repaired.
- Often toilet unavailable

Photos



	(6) Electricity	Improved□ Same ■* Worse □ *as last week	 Residents get the electricity regularly. Electric poles and transformer are being supported with the good foundations. There are some pieces of wood under an electric pole of main road B and it's needed to clean up. Photos		
			Transformer No. 1	Transformer No. 2	
			Transformer No. 3	Electric poles of Main Road B and Main Road C	
			Description and Photos		
No	Item	Condition	Description	and Photos	
No 2	(1)House Construction	No. of houses which are not completed (4)	 In plot No.9 and 10, three houses are owned by father and son. The are needed to be carried on. 	that are planned to build as the plots e second floors of these three houses on for the first floor has been finished	
	(1)House Construct-	No. of houses which are not	 In plot No.9 and 10, three houses are owned by father and son. The are needed to be carried on. Plot No. 66, the house construction 	that are planned to build as the plots e second floors of these three houses on for the first floor has been finished	
	(1)House Construct-	No. of houses which are not	 In plot No.9 and 10, three houses are owned by father and son. The are needed to be carried on. Plot No. 66, the house construction and the second floor is still needed. 	that are planned to build as the plots e second floors of these three houses on for the first floor has been finished	

3	Other Issues				
	(1). Drainage condition for	<u>Description</u>			
	rain water in the compounds	N CYWY			
		Condition	No. of HHs	Duovi 1	
		Condition	This week condition	Previous week condition	
		Level 1	82	82	
		Level 2	5	5	
		Level 3	3	3	
		Level 4	1	1	
			1 -		
		<evaluation c<="" th=""><th>Criteria></th><th></th><th></th></evaluation>	Criteria>		
		Level 1			
			standing water	with their own d	rainage system in their
		compound			
		Level 2	s standing water	in their compour	.d
		Level 3	standing water	in their compour	lu
			mud and standir	ng water in their o	compound
		Level 4		C	1
			nd standing wate	er in their compo	and
		D 1	1 01	45	1 11 1 1
					be muddy again as it has
		changed in the		nerefore the othe	r photo for level 3 will be
		changed in the i	ilext report.		
		Photos	THE PROPERTY OF THE PARTY OF		
		Level 1 House No. 3		Level	e No. 19
		Level 3 House No. 64		Level	e No. 84
		Level 3 House No. 7	5	Level	No. 88

(2) Plantation

In front of the compounds, the shady trees, fruit trees, flowering plants and vegetables are being planted.

Description

- In front of the compounds, the shade trees, fruit trees, flowering plants and vegetables are being planted.

Type	No. of	Remarks
	HHs	
Shade tree	15	Albizzia, Indian almond, Neem tree, etc.
		HH No. 20, 40, 43, 48, 51, 57, 59, 61, 62, 67,
		69, 72, 73, 77, 85
Fruit tree	37	Banana, Mango, sugar cane, coconut, citrus
		and jack fruit etc.
		HH No. 3, 15, 17, 20,21, 23, 28, 30, 31, 32, 34,
		37, 40, 41, 48, 51, 52, 55, 57, 58, 59, 61, 62,
		63, 67, 68, 70, 71, 72, 73, 77, 78, 82, 85, 86, 88
Vegetables	20	Chili, tomato, bitter gourd, Roselle, gourd,
		basils, eggplant etc.
		HH No. 12, 17, 21, 41, 49, 58, 59, 61, 62, 63,
		67, 68, 70, 71, 72, 73, 77, 82, 85, 86
Flowering	31	Jasmine, poinsettia, orchid, kiss me quick, etc.
plant		HH No. 3, 5, 6, 8, 10, 12, 13, 14, 17, 20, 21,
		22, 23, 29, 30, 31, 32, 46, 48, 58, 59, 61, 62,
		65, 67, 68, 69, 72, 77, 78, 86

Photos









(3) Livestock

Description

-The chicken, gooses and ducks are being raised.

Type	No. of HHs	Remarks
Chicken	6	HH No. 13, 14, 21,
		59, 67, 78
Duck	3	HH No.12
Goose	2	HH No. 40, 67

Photos



